Public Disclosure Authorized

Public Disclosure Authorized

GAS SECTOR EFFICIENCY IMPROVEMENT AND CARBON ABATEMENT PROJECT (P179009)

SOUTH ASIA | Bangladesh | IBRD/IDA | Investment Project Financing (IPF) | FY 2024 | Seq No: 5 | Archived on 18-Feb-2026 | ISR06909

1. OBJECTIVE

1.1 Development Objective

Original Development Objective (Approved as part of Approval package on 27-Jul-2023)

To improve efficiency of gas distribution and end-use, and support carbon abatement in the gas sector

Has the Development Objective been changed since Board Approval of the Project Objective?

No

2. COMPONENTS

Name
Strengthening the gas sector downstream monitoring and control capabilities:(Cost 433,730,000.00)
Technical assistance for carbon abatement of the oil and gas value chain:(Cost 4,010,000.00)

3. OVERALL RATINGS

Name	Previous	Current
Progress towards achievement of PDO	Satisfactory	Satisfactory
Overall Implementation Progress (IP)	Satisfactory	Moderately Satisfactory
Overall Risk Rating	Moderate	Substantial

4. KEY ISSUES & STATUS

4.1 Implementation Status and Key Decisions

Implementation of the Carbon Abatement Technical Assistance is progressing at full pace, with substantial advancements achieved in data collection, stakeholder engagement, and capacity-building activities, marking significant progress toward the achievement of the PDO.

5. SYSTEMATIC OPERATIONS RISK-RATING TOOL

Risk Category	Rating at Approval Approval Package - 27 Jul 2023	Last Approved Rating ISR Seq. 04 - 13 Jul 2025	Proposed Rating
Political and Governance	Moderate	Moderate	Substantial
Macroeconomic	Moderate	Moderate	Moderate
Sector Strategies and Policies	Moderate	Moderate	Moderate
Technical Design of Project or Program	Moderate	Moderate	Moderate
Institutional Capacity for Implementation and Sustainability	Substantial	Moderate	Moderate
Fiduciary	Substantial	Moderate	Moderate
Environment and Social	Moderate	Moderate	Moderate
Stakeholders	Moderate	Moderate	Low
Overall	Substantial	Moderate	Substantial

6. RESULTS

6.1 PDO Indicators by PDO Outcomes

Total greenhouse gas emissions avoided as a result of the Project (kT of CO2 equivalent)								
Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
Total greenhouse gas emissions avoided as a result of the Project (Metric ton)	0.00	Jun/2023	0.00	26-Mar-2025	0.00	26-Mar-2025	3,250.00	Jun/2028
	Comments on achieving targets		This will measure the total amount of avoided CO2 emissions because of the reduction in gas consumption from the installation of prepaid meters and reduction in non-technical losses from advanced monitoring infrastructure					
Projected gas savings: average amount of gas saved per meter								
Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
Projected gas savings: average amount of gas saved per meter (cubic meters) (Cubic Meter(m3))	0.00	Jun/2023	0.00	30-Nov-2025	0.00	30-Nov-2025	26.01	Jun/2028
	Comments on achieving targets		This will measure the average amount of monthly gas saved per meter in a kitchen with one double- burner kitchen as a result of the prepaid metering infrastructure.					
Action Plan for carbon abatement of sector operations								
Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
Endorsement of Action Plan for carbon abatement of sector operations (Yes/No)	No	Jun/2023	No	30-Nov-2025	No	30-Nov-2025	Yes	Jun/2028
	Comments on achieving targets		This will track the endorsement of an Action Plan for carbon abatement of sector operations by the MPEMR, the sector's main authority					
Roadmap for the development and implementation of a sector policy carbon abatement framework								
Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year

Endorsement of Roadmap for the development and implementation of a sector carbon abatement framework (Yes/No)	No	Jun/2023	No	30-Nov-2025	No	30-Nov-2025	Yes	Jun/2028
	Comments on achieving targets		This will track the endorsement of a Roadmap for the development and implementation of a sector policy, legal, institutional, regulatory and contractual framework for sector carbon abatement by the MPEMR					

6.2 Intermediate Results Indicators by Components


Strengthening the gas sector downstream monitoring and control capabilities								
Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
People with enhanced resilience to climate risks (Number of people) CRI	6,000,000	Mar/2024	600,000	11-Dec-2024	600,000	11-Dec-2024		Dec/2028
People with enhanced resilience to climate risks – Female (Number of people) CRI	100,000		100,000	11-Dec-2024	100,000	11-Dec-2024		
People with enhanced resilience to climate risks – Youth (Number of people) CRI	200,000	Mar/2024	200,000	11-Dec-2024	200,000	11-Dec-2024		
Annual CO2 emission reduction supported by the investments under the Project (Metric ton)	0.00	Jun/2023	0.00	31-Oct-2023	0.00	31-Oct-2023	650.00	Jun/2028
	Comments on achieving targets		This will measure the total amount of CO2 emissions reduced because of the reduction in gas consumption from the installation of prepaid meters and reduction in non-technical losses from advanced monitoring infrastructure					
	0.00	Jun/2023	0.00	31-Oct-2023	0.00	31-Oct-2023	1,228,000.00	Jun/2028

Number of prepaid meters installed for residential consumers (Number)	Comments on achieving targets		Number of pre-paid meters (card-based NFC type diaphragm meters and online- based ‘“smart”’ meters using ultrasonic measurement) installed for residential consumers in TGTDCL and PGCL service territories (Number)					
Number of smart meters installed for industrial customers (Number)	0.00	Jun/2023	0.00	31-Oct-2023	0.00	31-Oct-2023	50.00	Jun/2028
	Comments on achieving targets		Number of smart meters installed for industrial customers to undertake the pilot program					
Number of distribution companies provided with SCADA/GIS systems (Number)	0.00	Jun/2023	0.00	31-Oct-2023	0.00	31-Oct-2023	1.00	Jun/2028
	Comments on achieving targets		Number of regulating and metering stations provided with SCADA systems					
Person-Days of Training Provided to TGTDCL and PGCL staff (Days)	0.00	Jun/2023	0.00	31-Oct-2023	0.00	31-Oct-2023	2,000.00	Jun/2028
	Comments on achieving targets		This will measure the person-days of TGTDCL and PGCL staff (males and females) trained across different areas under the institutional and capacity-building component of the project.					
Person-Days of Training Provided to TGTDCL and PGCL female staff (Days)	0.00	Jun/2023	0.00	31-Oct-2023	0.00	31-Oct-2023	800.00	Jun/2028
	Comments on achieving targets		This sub-indicator will measure the person-days of TGTDCL and PGCL staff (females) trained across different areas under the institutional and capacity-building component of the project.					
Share of female university and polytechnic graduates recruited by TGTDCL and PGCL for 6-month paid internships (Percentage)	0.00	Jun/2023	0.00	31-Oct-2023	0.00	31-Oct-2023	40.00	Jun/2028
	Comments on achieving targets		TGTDCL and PGCL will establish new or expand existing internship programs to recruit female university and polytechnic institute graduates for 6-month paid internships to increase the pool of potential female applicants for permanent positions at both utilities					
Percentage of grievances related to the facility satisfactorily addressed within two months of receipt (Percentage)	0.00	Jun/2023	0.00	31-Oct-2023	0.00	31-Oct-2023	80.00	Jun/2028
	Comments on achieving targets		This will measure the percentage of grievances/ complaints received on the activities related to the project that are satisfactorily addressed within a period of two months from date of receipt.					
Technical assistance for carbon abatement of the oil and gas value chain								

Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
Person days of training on carbon abatement in Oil and Gas operations (Days)	0.00	Jun/2023	0.00	30-Sep-2025	0.00	30-Sep-2025	60.00	Jun/2028
	Comments on achieving targets		This will measure the Person-days of training on carbon abatement in O&G operations for staff of MPEMR, BERC, Petrobangla, and other subject-matter-relevant GoB personnel under component 2 of the project. It will target at least 60 person-days (20 participants x 3 1-day workshops)					
Person-days of training on legal and regulatory frameworks for carbon abatement in Oil and Gas operations (Days)	0.00	Jun/2023	0.00	30-Sep-2025	0.00	30-Sep-2025	20.00	Jun/2028
	Comments on achieving targets		This will measure the Person-days of training on carbon abatement in O&G operations for staff of MPEMR, BERC, Petrobangla and other subject-matter-relevant GoB personnel under component 2 of the project. It will target at least 20 person-days (10 participants x 2 1-day workshops)					

7. DATA ON FINANCIAL PERFORMANCE

7.1 Cumulative Disbursements

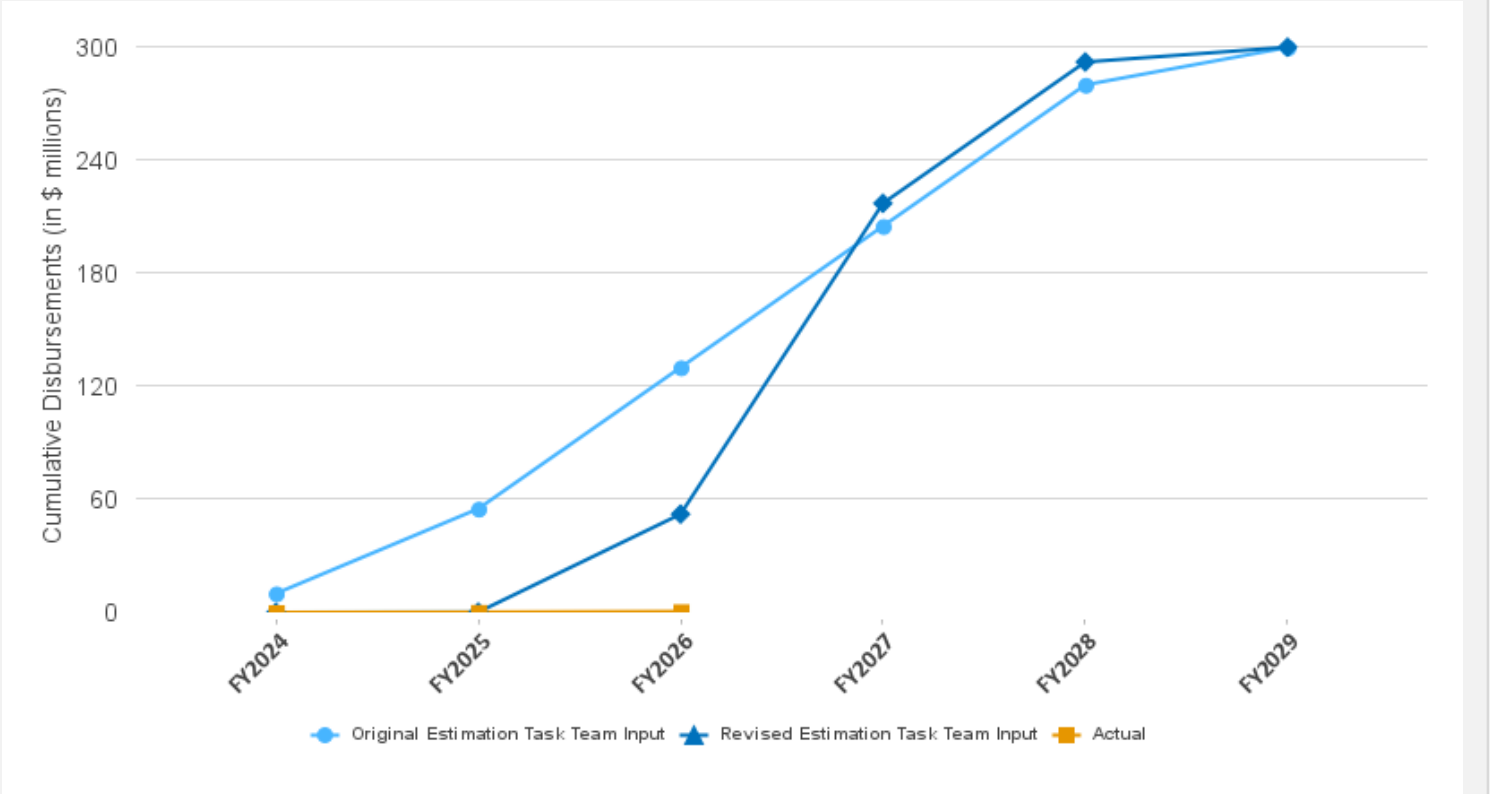

7.2 Disbursements (by loan)

Loan/Credit/TF	Status	Original	Revised	Cancelled	Disbursed	Undisbursed	Historical Disbursed	% Disbursed
IDA-73860	Effective	187.60	194.77	0.00	0.00	194.77	0.00	0%
IDA-73870	Effective	52.40	54.41	0.00	.17	54.24	.17	0.31%
IDA-73880	Effective	60.00	60.00	0.00	.44	59.56	.44	0.73%

7.3 Key Dates (by loan)

Loan/Credit/TF	Status	Approval	Signing	Effectiveness	Orig. Closing	Rev. Closing
IDA-73860	Effective	27-Jul-2023	22-Nov-2023	15-Feb-2024	31-Dec-2028	31-Dec-2028
IDA-73870	Effective	27-Jul-2023	22-Nov-2023	15-Feb-2024	31-Dec-2028	31-Dec-2028
IDA-73880	Effective	27-Jul-2023	22-Nov-2023	15-Feb-2024	31-Dec-2028	31-Dec-2028

8. KEY DATES

Key Events	Planned	Actual
Approval	27-Jul-2023	27-Jul-2023
Effectiveness	15-Feb-2024	15-Feb-2024
Operation Closing/Cancellation	31-Dec-2028	

9. RESTRUCTURING HISTORY

10. ASSOCIATED OPERATION(S)

There are no associated operations
